



**Resources
Regulator**

FWP0001844

HUNTER VALLEY OPERATIONS FORWARD PROGRAM

Thursday 1 January 2026 to Sunday 31 December 2028

Summary

Detail	
Mine	Hunter Valley Operations
Reference	FWP0001844
Forward program commencement date	Thursday 1 January 2026
Forward program end date	Sunday 31 December 2028
Forward program revision (if applicable)	
Contact	Darby O'Sullivan
Mining leases	ML 1705 (1992), ML 1748 (1992), ML 1869 (1992), ML 1871 (1992), ML 1622 (1992), ML 1474 (1992), ML 1811 (1992), CCL 755 (1973), ML 1526 (1992), ML 1704 (1992), ML 1849 (1992), ML 1841 (1992), ML 1870 (1992), CL 360 (1973), ML 1560 (1992), CCL 714 (1973), ML 1428 (1992), ML 1840 (1992), ML 1359 (1992), CL 584 (1973), ML 1732 (1992), ML 1589 (1992), CL 359 (1973), ML 1753 (1992), CL 327 (1973), ML 1482 (1992), CML 4 (1992), ML 1867 (1992), ML 1324 (1992), ML 1682 (1992), ML 1406 (1992), ML 1734 (1992), CL 398 (1973), ML 1706 (1992), ML 1634 (1992), ML 1710 (1992), ML 1707 (1992), ML 1465 (1992), ML 1500 (1992), ML 1337 (1992), ML 1810 (1992)

Project location	Anotero Pty Limited
Date of submission	Tuesday 31 March 2026
Document URL Security reminder: Please exercise caution before opening external links. If a link appears suspicious, avoid clicking it and report it to the Resources Regulator.	https://www.hvo.com.au/

Important

The department may make the information in your program and any supporting information available for inspection by members of the public, including by publication on its website or by displaying the information at any of its offices. If you consider any part of your program to be confidential, please communicate this to the department via the message function on this submission within the Resources Regulator Portal.

Three-year forecast - surface disturbance activities

Project description

Hunter Valley Operations (HVO) is situated in the Upper Hunter Valley between Singleton and Muswellbrook, approximately 24 km northwest of Singleton, and approximately 100 km northwest of Newcastle. The Hunter River geographically divides HVO into HVO North (DA 450-10-2003) and HVO South (PA_06_0261); however, they are integrated operationally with personnel, equipment and materials utilised as required. HVO is a jointly controlled operation through a Joint Venture (JV) between Glencore (49%) and Yancoal (51%). HVO North includes the Carrington Pit, West Pit (which includes the Mitchell Pit and Wilton Pit), North Pit Tailings Storage Facility (TSF), Dam 6W TSF, Hunter Valley Coal Preparation Plant (HVCPP), Howick Coal Preparation Plant (HCPP), and the stockpiling/train loading facilities at Newdell Load Point (NLP) and Hunter Valley Load Point (HVLP). HVO South includes Cheshunt Pit, Riverview Pit and Lemington South Pit.

Description of surface disturbance activities

Exploration activities

Exploration drilling will be undertaken within the HVO mining lease areas to obtain further information regarding the resources to be mined as well as define geological and geotechnical information relevant to the mining and construction activities that will be undertaken. Exploration activities during Year 1 will include up to approximately 57 holes.

Construction activities

Water Management: - Cheshunt Dam 39S Upgrade - Hunter River South sumps upgrades - Load Point water management works - North Void TSF barrier wall and Levee installation - New bioremediation area in HVO South Infrastructure: No major infrastructure planned in the next three years outside of planned infrastructure associated with the HVO Continuation Project which is currently pending regulatory approval.

Mining schedule

Mining development method and sequencing and general mine features.

Mining at HVO involves the following general sequence: • Pre-stripping the topsoil; • Removing the overburden (by shovel and excavators); • Coal mining (coal extraction by excavators and front-end loaders); and • Coal transport and processing. Mining will continue in accordance with current operational practices. Mining is currently carried out by shovels and excavators, supported by loaders, dozers, graders, water trucks and a fleet of dump trucks. Overburden and interburden is either free dug or drilled and blasted, removed using a combination of excavator/front end loaders/dozers and placed in trucks for haulage to out of pit emplacements or refill areas in the pit. During the next three years, open cut resources will be mined in the four main pit areas: * West Pit - mining will progress south-eastwards and reach its limit along Lemington Road; * Mitchell Pit - mining will initially progress in a south-western direction then in a south-east direction towards Lemington Road; * Cheshunt Pits - mining will progress in a westerly and southerly direction; and * Riverview Pit - mining will extend southwards towards the Golden Highway. Mining in the Carrington West Wing has not commenced and is not planned to commence in the next three years. The HVO Continuation Project (HVOCP) has been initialised to extend operations at HVO - if approved, mining in HVO North would extend from 2026 to 2050 and HVO South would extend from 2030 to 2045.

Areas identified for emplacements, the sequencing of emplacements, construction, and management.

All overburden and interburden material generated from mining operations at HVO is hauled to current emplacement areas behind the active mining operation. As part of the integration of operations at HVO, mining waste may be transported to any HVO pit for

emplacement to achieve the final approved landform. All mining waste emplacements shall be reshaped as required to construct a final landform. The method and height of emplacement areas shall be in accordance with the final approved landforms and HVO procedures for dumping. During the next three years, overburden emplacement will occur in the following main dump areas: * West Pit - West Pit North, Central and South dumps will continue to progress in an easterly direction, up to their maximum approved height; * Mitchell Pit - the Mitchell Pit dump will be developed to continue south from the Wilton dump; * Cheshunt Pit - the Cheshunt dump will continue to move west and be developed along its eastern and northern facing slopes up to its maximum approved height; and * Riverview Pit - the Riverview dump will continue to progress to the south behind the active mining area.

Processing infrastructure activities and the location of tailings facilities and schedule for emplacement.

Coal will continue to be processed at the Howick Coal Preparation Plant (HCPP) and Hunter Valley Coal Preparation Plant (HVCPP) during the next three years. Currently active tailings facilities include: * Cumnock Void - deposition from HCPP; and * Carrington In-pit - deposition from HVCPP. Dam 6W TSF has currently ceased deposition, however, it may be restarted in the next three years to provide a final top up to assist consolidation prior to capping activities. Other tailings storage facilities that are currently inactive or being capped at HVO include: * Central TSF - requires additional tailings deposition prior to capping; * Bobs Dump TSF - capping of stage 1 has been completed with stage 2 to be completed in the next three years; and * North Void TSF - ongoing implementation of the North Void TSF Management Plan to manage and mitigate any potential impacts from an identified seepage pathway. Construction of the barrier wall for the North Void TSF will commence in 2026.

Waste disposal and materials handling operations.

Recycling and disposal of waste at HVO focuses on the correct handling, storage, segregation and reuse of materials. Waste will be managed in accordance with the following waste management hierarchy principles: • Waste avoidance; • Waste re-use; • Waste recycling; and • Waste removal and disposal. A specialised oil and grease storage facility exists at all active service areas. The bulk oils and grease storage facilities are part of the fuel storage facility and meet Australian Standards. All waste hydrocarbons are collected and then recycled via a licensed waste hydrocarbon disposal company. HVO implements procedures and controls to minimise the

potential for land and water contamination from the handling, storage and disposal of hazardous substances. These controls include storage within properly sealed containers and controlled areas, bundled for medium to long-term storage requirements. Additional management measures include: • Inspecting and maintaining equipment and plant, including the conveyor networks regularly to minimise potential for leaks associated with equipment failures; • Management of identified asbestos at various buildings across HVO in accordance with the Asbestos Management Plan and Register; • Maintaining the existing bioremediation areas and establishing additional bioremediation areas as required to treat soils contaminated by hydrocarbon spills; and • Maintaining a Contaminated Sites Register.

Key production milestones

MATERIAL	UNIT	YEAR 1	YEAR 2	YEAR 3
Stripped topsoil (if applicable)	(m ³)	296.79	275.26	235.4
Rock/overburden	(m ³)	113.92	119.74	131.66
Ore	(Mt)	18.93	20.28	22.09
Reject material¹	(Mt)	4.37	5.11	6.07
Product	(Mt)	14.66	15.52	16.02

¹This includes coarse rejects, tailings and any other wastes resulting from beneficiation.

Three-year rehabilitation forecast

Rehabilitation planning schedule

Rehabilitation planning schedule

All areas disturbed as part of the operation will be progressively rehabilitated throughout the life of the mine. Each year HVO prepares a Life of Mine Plan (LOM) which outlines a high level plan for the following five years in regards to disturbance, mining, dumping and rehabilitation activities. Following review and approval of the LOM, an annual budget is prepared for the following calendar year which refines and provides further detail on the next calendar year. This is where rehabilitation planning commences as mining and dumping areas are confirmed. Resources are also allocated to ensure rehabilitation activities (shaping, ground preparation and seeding) can occur in a timely manner. This information is then formalised in an Annual Rehabilitation and Closure Plan which outlines: * areas available for rehabilitation; * areas of completed rehabilitation (progressed to Ecosystem and Land Use Establishment Phase); * areas of proposed disturbance (both new disturbance and rehabilitation disturbance); * methodologies for proposed rehabilitation activities; * resources required; and * rehabilitation maintenance activities.

Stakeholder consultation

HVO has consulted with relevant government agencies during the preparation of the Rehabilitation Management Plan (RMP). Further consultation will be undertaken for any future revisions of the RMP as required by DA-450-2003 and PA_06_0261. Consultation will occur with the Resource Regulator and Singleton Council on the preparation and subsequent revisions of the Rehabilitation Strategy as required by Schedule 2 condition 62C of DA-450-2003 HVO. Ongoing consultation is undertaken with the Community Consultative Committee (CCC). The CCC for HVO provides a forum for important community discussion with community representatives acting as the point of contact to provide feedback between HVO and near neighbours. The CCC is required to meet three times a year and discusses

operational plans for the operation including mining progress, proposed disturbance and proposed/completed rehabilitation. Additional consultation will be undertaken with relevant agencies in the next three years regarding the HVO Continuation Project.

Rehabilitation studies, risk assessments and/or design work

HVO has prepared an Operational Mine Closure Plan (OMCP) in line with internal guidelines to document a clear, well planned and executable mine closure process for HVO that will provide for a sustainable post-mining land use and ultimately allow mining tenements to be relinquished. Key components of the OMCP include a mine closure risk assessment (reviewed annually) and a schedule of future studies required to confirm / close knowledge gaps related to specific mine closure aspects. plan. Refinement of the final landform drainage design will also continue over the next three years . This is an ongoing process where a conceptual design is prepared, and then updated following completion of dumping activities. The drainage infrastructure is then constructed and compliance to design is assessed and fed back into the design for the next section of rehabilitation. The final landform will also be updated pending a decision on the regulatory approval of the HVO Continuation Project. Additionally, ongoing work is continuing in the next three years in regard to the development of capping and rehabilitation strategies for the following tailings storage facilities: *Bobs Dump Stage 2; *North void TSF; * Central TSF; * Dam 6WTSF; and * Carrington TSF

Rehabilitation research and trials

RRT NUMBER	PROJECT/TRIAL NAME	OBJECTIVE OF TRIAL/PROJECT	METHODOLOGY	EXPECTED DATE OF COMPLETION	STATUS
RRT0001170	Dam 6W Tailings Desiccation Enhancement Using Tubestock Planting	Experiments will be started in 2026 to test the dewatering capacity of tailings by vegetation.	Dam 6W will be planted with tubestock in 2026 to evaluate tailings amelioration techniques to maximise success for the native vegetation used.	31 Dec 2028	Ongoing

Rehabilitation maintenance and corrective actions

Rehabilitation maintenance requirements are identified through: * Annual Rehabilitation Walkover assessment; * Annual Rehabilitation Ecological monitoring; and * Assessment against the Rehabilitation TARP and completion criteria. All of these assessments include a range of specific maintenance activities for each rehabilitation block, as well as recommendations for improvements to the rehabilitation methodologies (where appropriate). Key maintenance works that are included in the recommendations include: * Weed control works; * Erosion repairs; * Re-seeding of failed areas; * Supplementary planting of target species or stratum missing from the target community; and * Pest animal control. Recommendations and maintenance requirements are then consolidated into a rehabilitation maintenance schedule which lists all required maintenance activities across the site. Maintenance works are also prioritised based on the level of risk to establishment and meeting closure criteria. Implementation is then tracked throughout the year and completed maintenance activities are marked as completed and removed from the schedule.

Rehabilitation schedule

As per the Rehabilitation planning schedule, an Annual Rehabilitation and Closure Plan is developed based on LOM and budget assessments to ensure all available rehabilitation is completed as soon as practical. Key rehabilitation activities over the next three years include: * West Pit - progressive rehabilitation on the West Central and Bob's Dump; and * Cheshunt Pit - progressive rehabilitation of the east and north facing dump slopes. It should be noted that the Total New Active Disturbance Area During Reporting Period hectares in this report include rehabilitation disturbance areas. The total new and rehabilitation disturbance areas for the next three years are as follows: * Year 1 – 16.5ha new disturbance and 107.8ha rehabilitation disturbance * Year 2 - 0ha new disturbance and 84.1ha rehabilitation disturbance * Year 3 – 80.5ha new disturbance and 59.9ha rehabilitation disturbance

Completion of rehabilitation

Not applicable.

Subsidence remediation for underground operations

Not applicable.

Progressive mining and rehabilitation statistics

Three-yearly forecast cumulative disturbance and rehabilitation progression

Forecast		UNIT	YEAR 1	YEAR 2	YEAR 3
A1	Total disturbance footprint - surface disturbance	(ha)	7,434.12	7,524.89	7,551.3
O	Total active disturbance	(ha)	4,430.55	4,495.77	4,496.5
P	Total new area of land proposed for active rehabilitation	(ha)	12.13	37.68	63.36

Rehabilitation key performance indicators (KPIs)

Forecast		UNIT	YEAR 1	YEAR 2	YEAR 3
O	Total new disturbance area during reporting period	(ha)	62.18	90.77	26.4
P	Total new area of land proposed for rehabilitation during the reporting period	(ha)	12.13	25.55	25.67
Q	Annual rehabilitation to disturbance ratio		0.2	0.28	0.97

Attachment 1 - Reporting Definitions

REPORTING CATEGORY		DEFINITION
A	Total disturbance footprint - surface disturbance	All areas within a mining lease that either have at some point in time or continue to pose a rehabilitation liability due to surface disturbance activities. The total disturbance footprint is the sum of the total active disturbance, decommissioning, landform establishment, growth medium development, ecosystem and land use establishment, ecosystem and land use development and rehabilitation completion (see definitions below). Underground mining operations should not include the footprint of underground mining areas/subsidence management areas in the total disturbance footprint.
B	Total active disturbance	Includes on-lease exploration areas, stripped areas ahead of mining, infrastructure areas, water management infrastructure, sewage treatment facilities, topsoil stockpile areas, access tracks and haul roads, active mining areas, waste rock emplacements (active/unshaped/in or out-of-pit), tailings dams (active/unshaped/uncapped) and temporary stabilised areas (e.g. areas sown with temporary cover crops for dust mitigation and temporary rehabilitation).
C	Rehabilitation - land preparation	Includes the sum of all disturbed land within a mining lease that have commenced

REPORTING CATEGORY		DEFINITION
		any, or all, of the following phases of rehabilitation - decommissioning, landform establishment and growth medium development. Refer to the glossary of terms in this document for the definition of these phases of rehabilitation.
D	Ecosystem and land use establishment	Includes the area which has been seeded/planted with the target vegetation species for the intended final land use. However, vegetation has not matured to a stage where it can be demonstrated that it will be sustainable for the long term and or require only a maintenance regime consistent with target reference/analogue sites. Typically, rehabilitation areas would be in this phase for at least two years (and usually more) before rehabilitation can be classified as being in the ecosystem and land use development phase. This phase does not apply to infrastructure areas that are being retained as part of final land use for the site.
O		The area of any new active disturbance that will be created during the next three years, as defined under definition A1 (definition A1 Table 5).
P		The sum of any new rehabilitation to be commenced in the next three years. These areas may be in the phases "Rehabilitation - Land Preparation" or the "Ecosystem & Land Use Establishment" (definitions C & D in Table 5).

REPORTING CATEGORY	DEFINITION
--------------------	------------

Q	The rehabilitation to disturbance ratio (S / R) indicates how many hectares of new rehabilitation are undertaken for each hectare of land disturbed during the three years. A ratio of 1/1 indicates that the area of new rehabilitation and disturbance in that period are the same.
---	---

Attachment 2 - Definitions

WORD	DEFINITION
Active	In the context of rehabilitation, land associated with mining domains is considered 'active' for the period following disturbance until the commencement of rehabilitation.
Active mining phase of rehabilitation	In the context of rehabilitation, the active mining phase of rehabilitation constitutes the rehabilitation activities undertaken during mining operations such as salvaging and managing soil resources, salvaging habitat resources, and native seed collection. This phase also includes management actions taken during operations to manage risks to rehabilitation and enhance rehabilitation outcomes such as selective handling of waste rock and management of tailings emplacements.
Analogue site	In the context of rehabilitation, an analogue site is a 'reference site' that represents an example of the defining characteristics (such as vegetation composition and structure or agricultural productivity) of the final land use. Characteristics of analogue sites can be assessed to develop the rehabilitation objectives and completion criteria for final land use domains.
Annual rehabilitation report and forward program	As described in the Mining Regulation 2016.
Annual reporting period	As defined in the Mining Regulation 2016.

WORD	DEFINITION
Closure	A whole-of-mine-life process, which typically culminates in the relinquishment of the mining lease. It includes decommissioning and rehabilitation to achieve the approved final land use(s).
Decommissioning	The process of removing mining infrastructure and removing contaminants and hazardous materials.
Decommissioning Phase of Rehabilitation	Activities associated with the removal of mining infrastructure and removal and/or remediation of contaminants and hazardous materials. In the context of the rehabilitation management plan this phase of rehabilitation may also include studies and assessments associated with decommissioning and demolition of infrastructure or works carried out to make safe or 'fit for purpose ' built infrastructure to be retained for future use(s) following lease relinquishment.
Department	Department of Primary Industries and Regional Development.
Disturbance	See Surface Disturbance.
Disturbance area	An area that has been disturbed and that requires rehabilitation. This may include areas such as on-licence exploration areas, stripped areas ahead of mining, infrastructure areas, water management infrastructure, sewage treatment facilities, topsoil stockpile areas, access tracks and haul roads, active mining areas, waste emplacements (active/unshaped/in or out-of-pit), tailings dams (active/unshaped/uncapped), and areas requiring rehabilitation that are temporarily stabilised (i.e. managed to minimise dust generation and/or erosion).

WORD	DEFINITION
Domain	An area (or areas) of the land that has been disturbed by mining and has a specific operational use (mining domain) or specific final land use (final land use domain). Land within a domain typically has similar geochemical and/or geophysical characteristics and therefore requires specific rehabilitation activities to achieve the associated final land use.
Ecosystem and Land Use Development	This phase of rehabilitation consists of the activities to manage maturing rehabilitation areas on a trajectory to achieving the approved rehabilitation objectives and completion criteria. For vegetated land uses this phase may include processes to develop characteristics of functional self-sustaining ecosystems, such as nutrient recycling, vegetation flowering and reproduction, and increasing habitat complexity, and development of a productive, self-sustaining soil profile. This phase of rehabilitation may include specific vegetation management strategies and maintenance such as tree thinning, supplementary plantings and weed management.
Ecosystem and Land Use Establishment	This phase of rehabilitation consists of the processes to establish the approved final land use following construction of the final landform. For vegetated land uses this rehabilitation phase includes establishing the desired vegetation community and implementing land management activities such as weed control. This phase of rehabilitation may also include habitat augmentation such as installation of nest boxes.
Exploration	Has the same meaning as that term under the State Environmental Planning Policy (Mining,

WORD	DEFINITION
	Petroleum Production and Extractive Industries) 2007.
Final landform and rehabilitation plan	As defined in the Mining Regulation 2016.
Final land use	As defined in the Mining Regulation 2016.
Form and way	Means the form and way approved by the Secretary. Approved form and way documents are available on the department's website.
Growth Medium Development	This phase of rehabilitation consists of activities required to establish the physical, chemical and biological components of the substrate required to establish the desired vegetation community (including short lived pioneer species. This phase may include spreading the prepared landform with topsoil and/or subsoil and/or soil substitutes, applying soil ameliorants to enhance the physical, chemical and biological characteristics of the growth media, and actions to minimise loss of growth media due to erosion.
Habitat	Has the same meaning as that term under the Biodiversity Conservation Act 2016 and the Fisheries Management Act 1994 (as relevant).
Indicator	An attribute of the biophysical environment (e.g. pH, topsoil depth, biomass) that can be used to approximate the progression of a biophysical process. It can be measured and audited to demonstrate (and track) the progress of an aspect of rehabilitation towards a desired completion

WORD	DEFINITION
	criterion (i.e. defined end point). It may be aligned to an established protocol and used to evaluate changes in a system.
Land	As defined in the Mining Act 1992.
Landform Establishment	This phase of rehabilitation consists of the processes and activities required to construct the final landform. In addition to profiling the surface of rehabilitation areas to the approved final landform profile this phase may include works to construct surface water drainage features, encapsulate problematic materials such as tailings, and prepare a substrate with the desired physical and chemical characteristics (e.g. rock raking or ameliorating sodic materials).
Large mine	As defined in the Mining Regulation 2016.
Lease holder	The holder of a mining lease.
Life of mine	The timeframe of how long a mine is approved to mine, from commencement to closure.
Mine rehabilitation portal	Means the Resources Regulator's online portal that lease holders must use (via a registered account) to:

WORD	DEFINITION
	• upload rehabilitation geographical information system (GIS) spatial data • develop rehabilitation GIS spatial data (using online tracing functions) • generate rehabilitation plans and rehabilitation statistics using the map viewer and Rehabilitation Key Performance Indicator functionalities. Data submitted to the mine rehabilitation portal is collated in a centralised geodatabase for use by the Resources Regulator to regulate rehabilitation performance of lease holders.
Mining area	As defined in the Mining Act 1992.
Mining domain	A land management unit with a discrete operational function (e.g. overburden emplacement), and therefore similar geophysical characteristics, that will require specific rehabilitation treatments to achieve the final land use(s).
Mining land	As defined in the Mining Act 1992.
Native vegetation	Has the same meaning as that term under section 60B of the Local Land Services Act 2013.
Overburden	Material overlying coal or a mineral deposit.
Performance indicator	An attribute of the biophysical environment (for example pH, slope, topsoil depth, biomass) that can be used to demonstrate achievement of a rehabilitation objective. It can be measured and audited to

WORD	DEFINITION
	demonstrate (and track) the progress of an aspect of rehabilitation towards a desired completion criterion, that is, a defined end point. It may be aligned to an established protocol and used to evaluate changes in a system.
Phases of rehabilitation	The stages and sequences of actions required to rehabilitate disturbed land to achieve the final land use. The phases of rehabilitation are: • active mining • decommissioning • landform Establishment • growth medium development • landform Establishment • ecosystem and land use establishment • ecosystem and land use development
Progressive rehabilitation	The progress of rehabilitation towards achieving the approved rehabilitation completion criteria. This may be described in terms of domains, phases, performance indicators and rehabilitation completion criteria.
Rehabilitation Completion	The final phase of rehabilitation when a rehabilitation area has achieved the approved rehabilitation objectives and rehabilitation completion criteria for the final land use. Rehabilitation areas may be classified as complete when the Resources Regulator has determined in writing that the relevant

WORD	DEFINITION
	rehabilitation obligations have been fulfilled following submission of <i>Form ESF2 Rehabilitation completion and/or review of rehabilitation cost estimate application</i> by the lease holder.
Rehabilitation Completion criteria	As defined in the Mining Regulation 2016.
Rehabilitation cost estimate	As defined in the Mining Regulation 2016.
Rehabilitation management plan	As defined in the Mining Regulation 2016.
Rehabilitation objectives	As defined in the Mining Regulation 2016.
Rehabilitation risk assessment	As defined in the Mining Regulation 2016.
Rehabilitation schedule	The defined timeframes for progressive rehabilitation set out in the forward program.
Relevant stakeholders	Means any persons or bodies who may be affected by the mining operations, including rehabilitation, carried out on the lease land, and includes: • the relevant development consent authority • the local council • the relevant landholder(s) • community consultative committee (if required under the development consent) or equivalent

WORD	DEFINITION
	consultative group • affected land holder(s) • government agencies relevant to the final land use • affected infrastructure authorities (electricity, telecommunications, water, pipeline, road, rail authorities) • local Aboriginal communities, and • any other person or body determined by the Minister to be a relevant stakeholder in relation to a mining lease.
Risk	The effect of uncertainty on objectives. It is measured in terms of consequences and likelihood (AS/NZS ISO 31000:2009).
Secretary	The Secretary of the department.
Security deposit	An amount that a mining lease holder is required to provide and maintain under a mining lease condition, to secure funding for the fulfilment of obligations under the lease (including obligations that may arise in the future).
Surface disturbance	Includes activities that disturb the surface of the mining area, including mining operations, ancillary mining activities and exploration.

WORD	DEFINITION
Tailings	A combination of the fine-grained solid material remaining after the recoverable metals and minerals have been extracted from the mined ore, and any process water ² .
Waste	Has the same meaning as that term under the <i>Protection of the Environment Operations Act 1997</i> .

²Commonwealth of Australia (DITR), 2007. Tailings Management.

Attachment 3 - Plans


Plan 2A Mining and Rehabilitation Year 1.zip

Plan 2B Mining and Rehabilitation Year 2.zip

Plan 2C Mining and Rehabilitation Year 3.zip

Hunter Valley Operations

Plan 2A: Mining and Rehabilitation - Year 1 (HVO North)

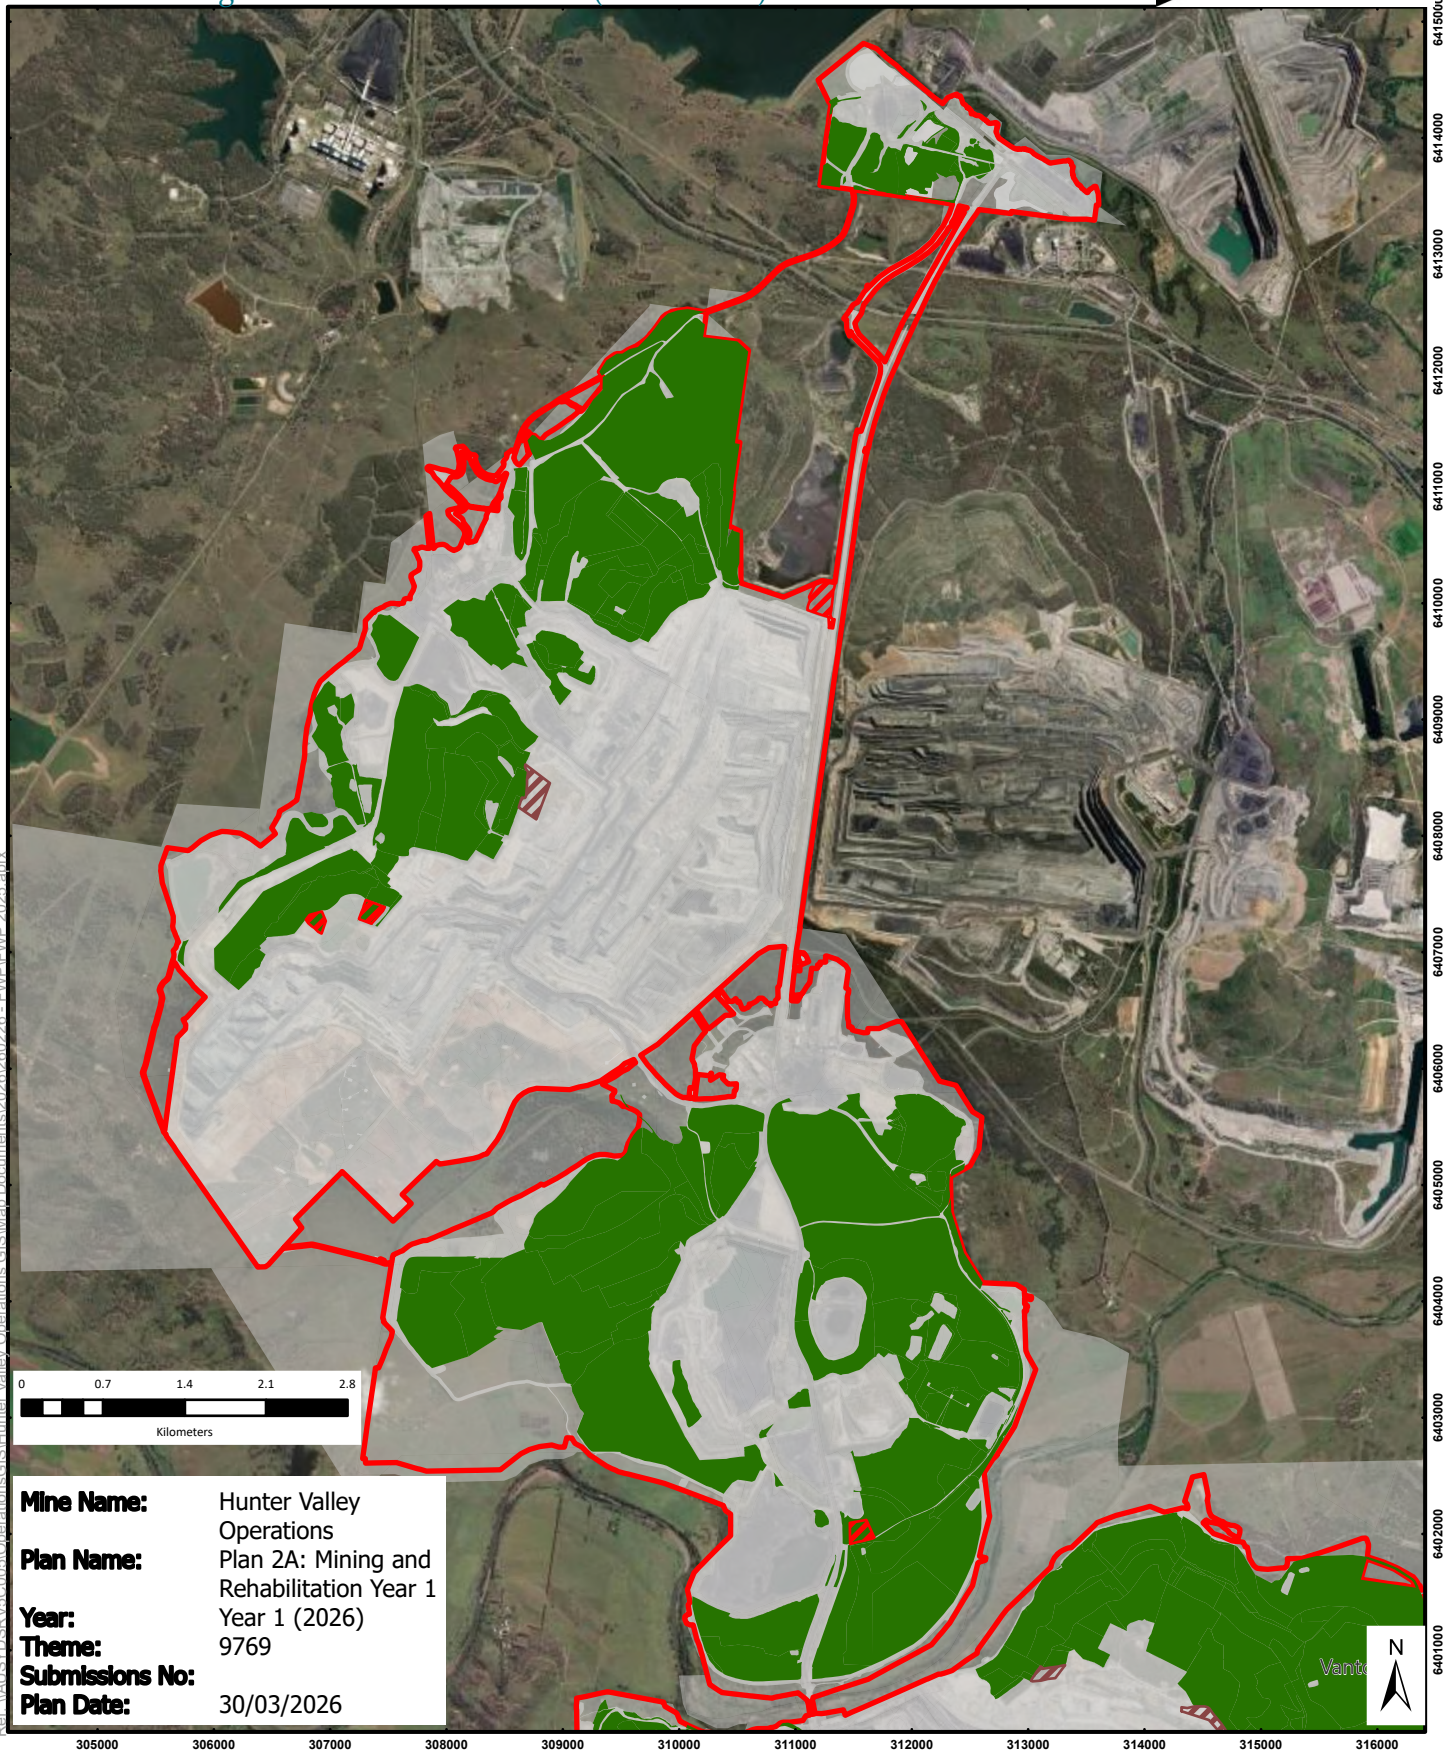

Mine Name: Hunter Valley Operations
Plan Name: Plan 2A: Mining and Rehabilitation Year 1
Year: Year 1 (2026)
Theme: 9769
Submissions No:
Plan Date: 30/03/2026

Legend:


- Forecast Disturbance
- Existing Disturbance
- Existing Rehabilitation
- HVO Project Approval Boundary
- Current Authorities



Date Created: 30/03/2026
 Map Size: A4 Portrait
 Scale: 1:65,000
 Map Created By: mfreeman3
 Coordinate System: GDA2020 MGA Zone 56
 Projection: Transverse Mercator

Hunter Valley Operations

Plan 2A: Mining and Rehabilitation - Year 1 (HVO South)

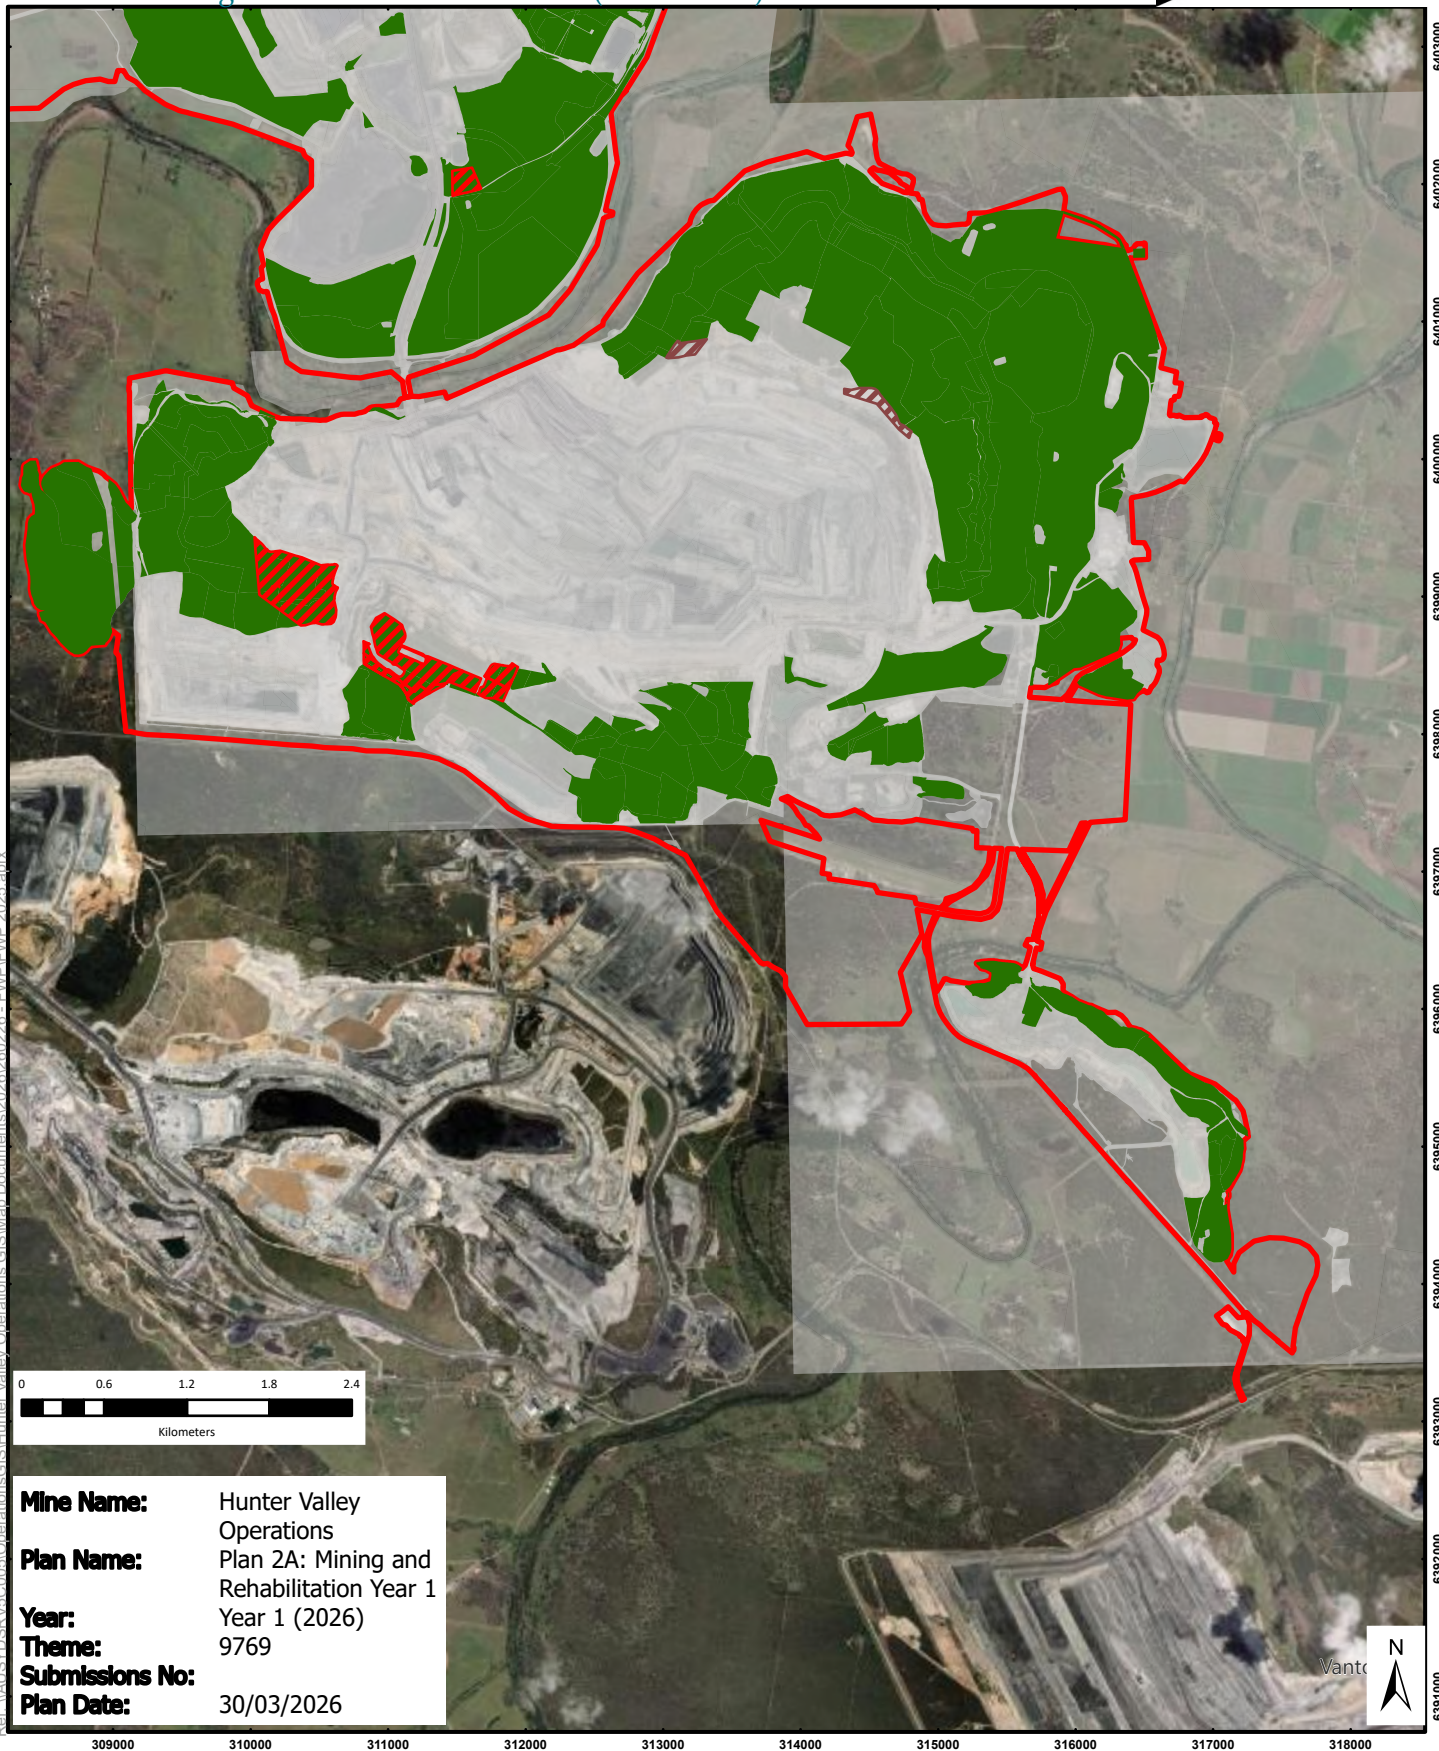

Mine Name: Hunter Valley Operations
Plan Name: Plan 2A: Mining and Rehabilitation Year 1
Year: 2026
Theme: 9769
Submissions No:
Plan Date: 30/03/2026

Legend:


- | | |
|--|---|
|  Forecast Disturbance |  HVO Project Approval Boundary |
|  Forecast Land Prepared for Rehabilitation |  Existing Disturbance |
|  Existing Rehabilitation |  Current Authorities |



Date Created: 30/03/2026
Map Size: A4 Portrait
Scale: 1:55,000
Map Created By: mfreeman3
Coordinate System:
GDA2020 MGA Zone 56
Projection: Transverse Mercator

Hunter Valley Operations

Plan 2B: Mining and Rehabilitation - Year 2 (HVO North)

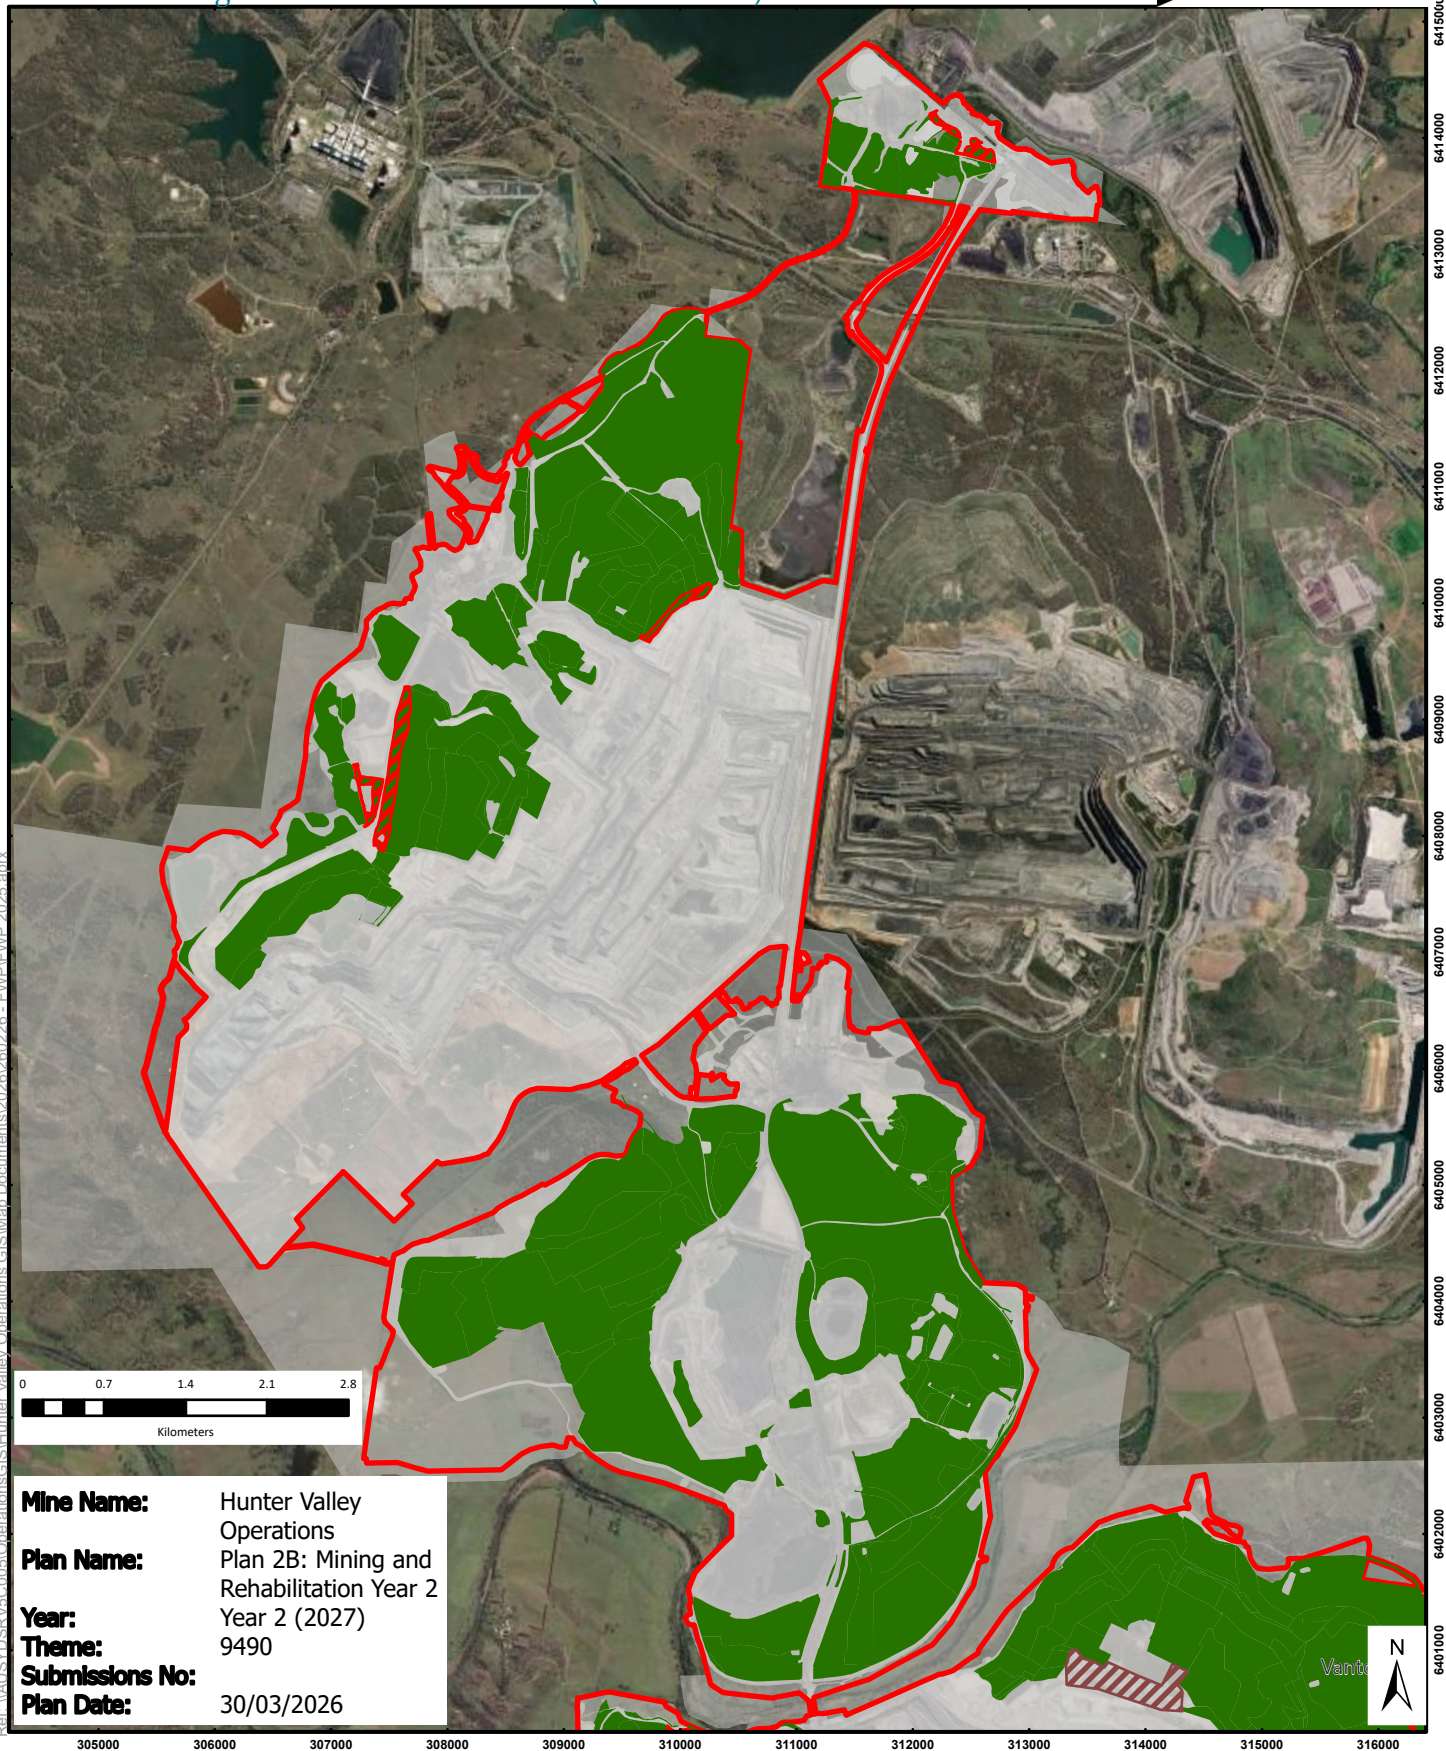

Mine Name: Hunter Valley Operations
Plan Name: Plan 2B: Mining and Rehabilitation Year 2
Year: Year 2 (2027)
Theme: 9490
Submissions No:
Plan Date: 30/03/2026

Legend:


- Existing Rehabilitation
- HVO Project Approval Boundary
- Existing Disturbance
- Current Authorities
- Forecast Disturbance
- Forecast Land Prepared for Rehabilitation



Date Created: 30/03/2026
 Map Size: A4 Portrait
 Scale: 1:65,000
 Map Created By: mfreeman3
 Coordinate System: GDA2020 MGA Zone 56
 Projection: Transverse Mercator

Hunter Valley Operations

Plan 2B: Mining and Rehabilitation - Year 2 (HVO South)

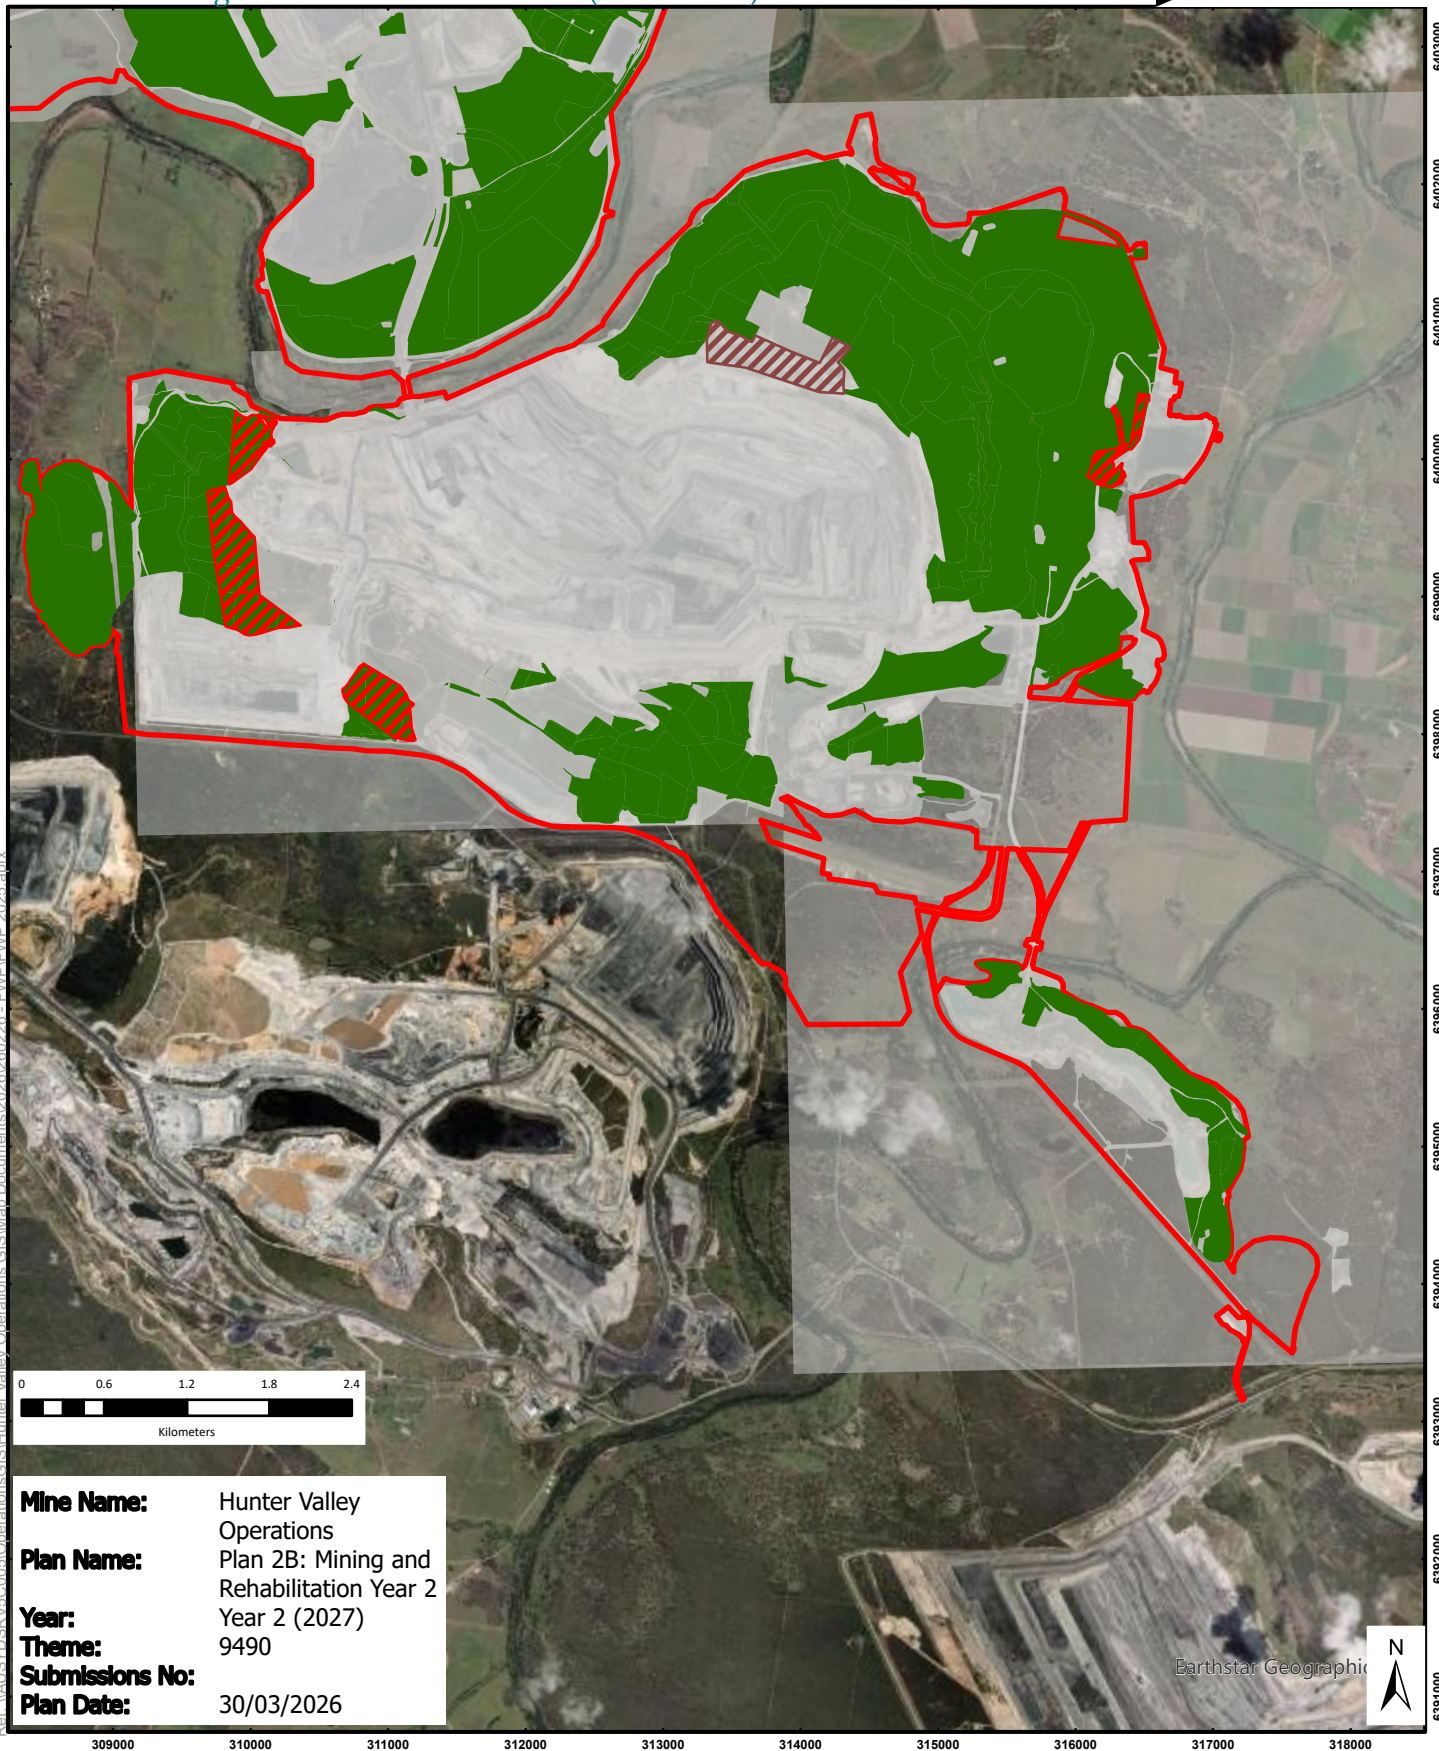

Mine Name: Hunter Valley Operations
Plan Name: Plan 2B: Mining and Rehabilitation Year 2
Year: Year 2 (2027)
Theme: 9490
Submissions No:
Plan Date: 30/03/2026

Legend:

- | | |
|-------------------------------|---|
| Existing Rehabilitation | Current Authorities |
| HVO Project Approval Boundary | Forecast Disturbance |
| Existing Disturbance | Forecast Land Prepared for Rehabilitation |




Date Created: 30/03/2026
Map Size: A4 Portrait
Scale: 1:55,000
Map Created By: mfreeman3
Coordinate System: GDA2020 MGA Zone 56
Projection: Transverse Mercator

DISCLAIMER: Subject To Survey. Glencore makes every effort to ensure the quality of the information available on this map. Before relying on the information on this map, users should carefully evaluate its accuracy, currency, completeness and relevance for their purposes, and should obtain any appropriate professional advice relevant to their particular circumstances. Glencore cannot guarantee and assumes no responsibility for the accuracy, currency or completeness of the information and by using this map you accept that Glencore has no liability for any loss or damage in any form whatsoever caused directly or indirectly from the use of this map.

DATA SOURCE: © NSW Department of Finance, Services & Innovation 2022; © NSW Dept. of Planning and Environment (Division of Resources & Geoscience) 2022; © Glencore 2022

Hunter Valley Operations

Plan 2C: Mining and Rehabilitation - Year 3 (HVO North)

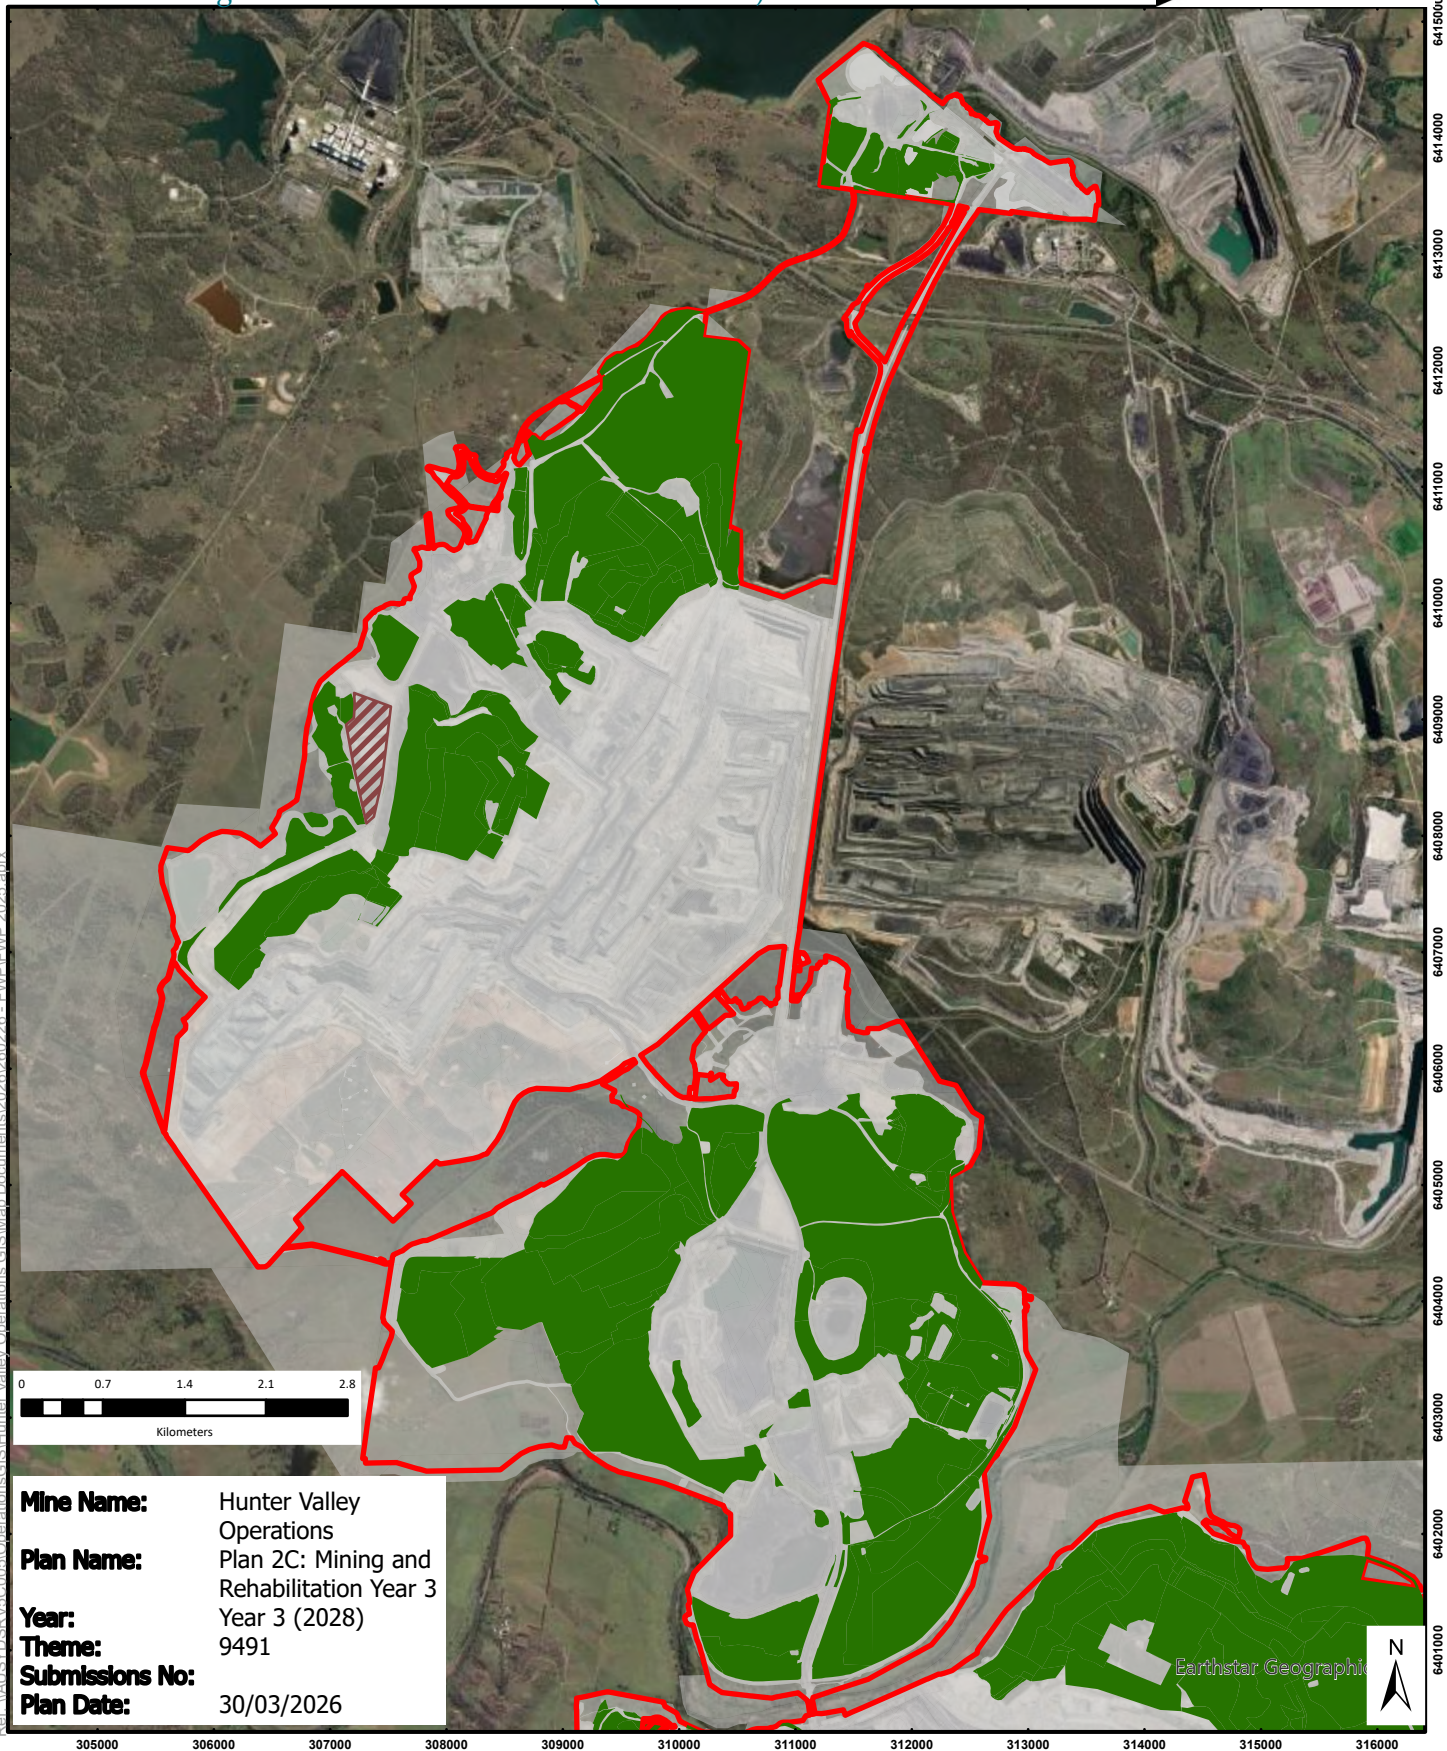

Mine Name: Hunter Valley Operations
Plan Name: Plan 2C: Mining and Rehabilitation Year 3
Year: Year 3 (2028)
Theme: 9491
Submissions No:
Plan Date: 30/03/2026

Legend:


- Existing Rehabilitation
- HVO Project Approval Boundary
- Existing Disturbance
- Current Authorities
- Forecast Disturbance
- Forecast Land Prepared for Rehabilitation



Date Created: 30/03/2026
 Map Size: A4 Portrait
 Scale: 1:65,000
 Map Created By: mfreeman3
 Coordinate System: GDA2020 MGA Zone 56
 Projection: Transverse Mercator

Hunter Valley Operations

Plan 2C: Mining and Rehabilitation - Year 3 (HVO South)

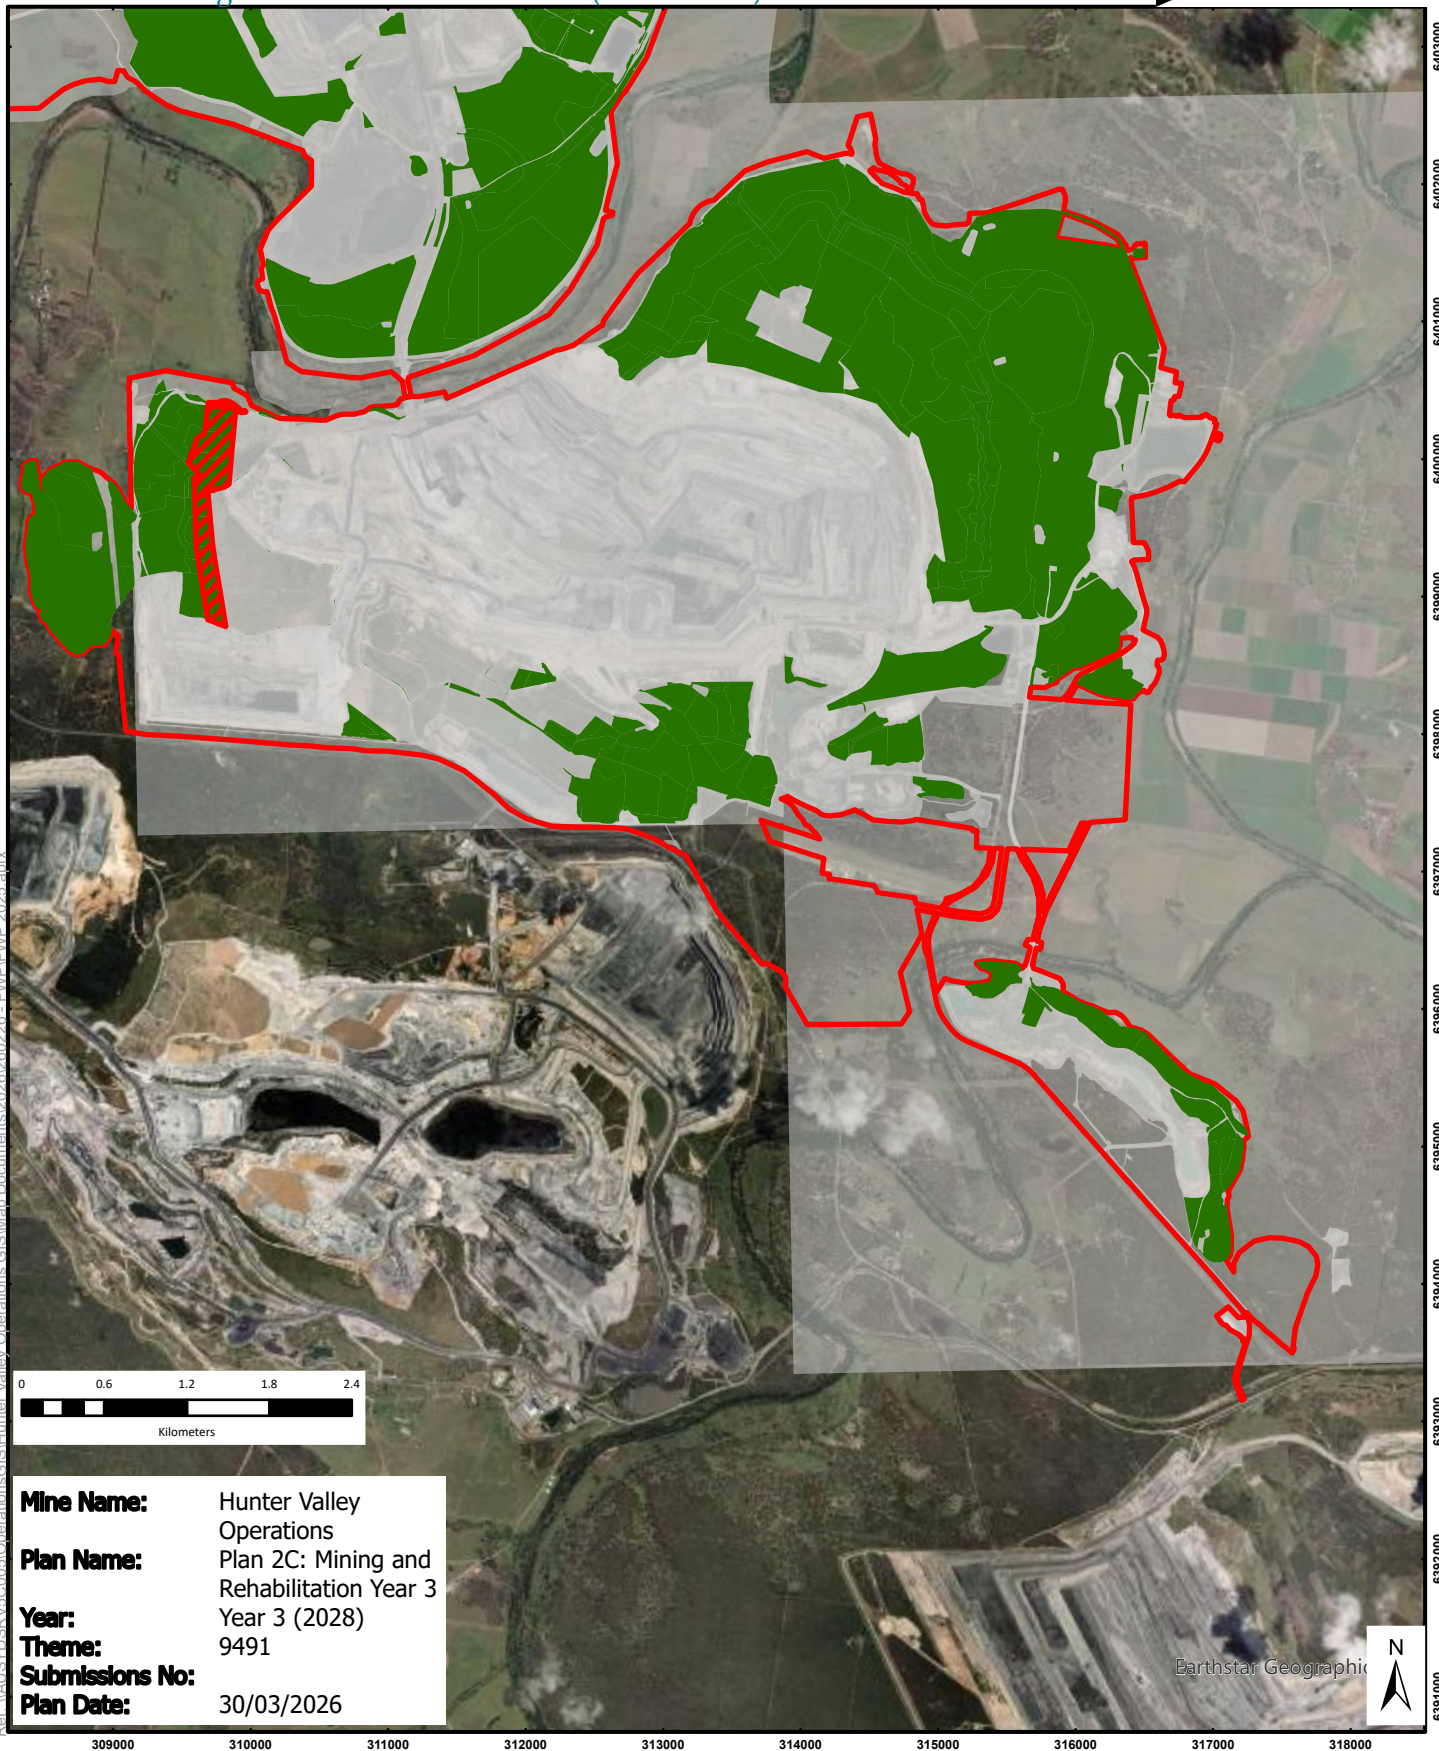

Mine Name: Hunter Valley Operations
Plan Name: Plan 2C: Mining and Rehabilitation Year 3
Year: 2028
Theme: 9491
Submissions No:
Plan Date: 30/03/2026

Legend:

- | | |
|--|---|
|  Existing Rehabilitation |  Current Authorities |
|  HVO Project Approval Boundary |  Forecast Disturbance |
|  Existing Disturbance |  Forecast Land Prepared for Rehabilitation |



Date Created: 30/03/2026
Map Size: A4 Portrait
Scale: 1:55,000
Map Created By: mfreeman3
Coordinate System:
GDA2020 MGA Zone 56
Projection: Transverse Mercator

Jointly held by Coal & Allied Operations Pty Ltd & Anotero Pty Limited - Hunter Valley Operations - HVO North

SITE REGISTRATION

Complete the following fields prior to calculating the Security Deposit.

Date of Estimate	31-Dec-25	Mine Name	Hunter Valley Operations - HVO North
Lease(s):	CL384, CL395, CL396, CL1735, CL1647, ML1476, ML1335, ML1482, ML1300, ML1320, ML1300, ML1385, ML1703, ML1700, ML1324, ML1704, ML1707, ML1426, ML1746, ML1811, ML1733, ML1871, ML1867, ML1860, ML1840, ML1841, ML1870, ML1730, ML1633, ML1406, ML1337		
Lease Holder(s):	Jointly held by Coal & Allied Operations Pty Ltd & Anotero Pty Limited		
Term of RCE:	12 months	This is period of time over which the RCE amount will apply.	
Date of last Security Deposit Review:	30-Mar-25	This is the date of the most recent correspondence from the Department advising of the assessed deposit amount.	
Amount of the last Security Deposit Review:	\$ 188,835,000.00	This is the most recent assessed deposit amount as per the most recent correspondence from the Department (see above).	
Current Security Deposit held by the Department:	\$ 188,835,000.00	This is the current security deposit amount held by the Department.	
List key changes since previous submission:	No significant changes mining footprint. Increase generally attributable to updated rates and domain calculations.		

Mining Domain Type	
Infrastructure Area	
Infrastructure - Mine Entries	
Beneficiation Facility	
Tailings Storage Facilities	
Water Management Area	
Overburden Emplacement Area	
Active Mining Area (Open Cut Void)	
Underground Mining Areas	
Exploration	Sub-total
Additional Items	
Other and Sundry	Sub-total
Totals	
Subtotal - all except Exploration	
Subtotal - Exploration	Subtotal - all
Contingency (Mining)	
Contingency (Exploration only)	Contingency Total
Grand Total (excluding GST)	

Cost	Comments
\$ 24,914,619	
\$ -	
\$ 27,982,335	
\$ 48,927,482	
\$ 7,844,636	
\$ 41,341,731	
\$ 10,546,572	
\$ -	
\$ 26,954	
\$ 161,584,328	
Cost	
\$ 4,908,790	
\$ 4,908,790	
\$ 166,466,164	
\$ 26,954	
r \$ 166,493,118	
\$ 49,939,849	Enter reason here if contingency greater than default is entered
\$ 4,043	Enter reason here if contingency greater than default is entered
\$ 49,943,892	
\$ 216,437,011	

Contingency for mining activities ok
Contingency for exploration activities ok

Rehabilitation Cost Estimate Tool - Mining New South Wales
Jointly held by Coal & Allied Operations Pty Ltd & Anotero Pty Limited - Hunter Valley Operations - HVO South

RCE Summary

SITE REGISTRATION

Complete the following fields prior to calculating the Security Deposit.

Date of Estimate	31-Dec-25	Mine Name	Hunter Valley Operations - HVO South
Lease(s):	CCL714, CL327, CL398, ML1465, ML1634, ML1682, ML1734, ML1753, ML1810		
Lease Holder(s):	Jointly held by Coal & Allied Operations Pty Ltd & Anotero Pty Limited		
Term of RCE:	12 months	This is period of time over which the RCE amount will apply.	
Date of last Security Deposit Review:	15-Aug-25	This is the date of the most recent correspondence from the Department advising of the assessed deposit amount.	
Amount of the last Security Deposit Review:	\$ 77,238,000.00	This is the most recent assessed deposit amount as per the most recent correspondence from the Department (see above).	
Current Security Deposit held by the Department:	\$ 77,238,000.00	This is the current security deposit amount held by the Department.	
List key changes since previous submission:	No significant changes mining footprint. Decreasegenerally attributable to updated rates and domain calculations.		

COST SUMMARY

Mining Domain Type		Cost	Comments
Infrastructure Area		\$ 13,267,360	
Infrastructure - Mine Entries		\$ -	
Beneficiation Facility		\$ -	
Tailings Storage Facilities		\$ -	
Water Management Area		\$ 2,792,885	
Overburden Emplacement Area		\$ 30,454,248	
Active Mining Area (Open Cut Void)		\$ 8,292,930	
Underground Mining Areas		\$ -	
Exploration		\$ 18,686	
Sub-total		\$ 54,846,109	
Additional Items		Cost	
Other and Sundry		\$ 2,983,015	
Sub-total		\$ 2,983,015	
Totals			
Subtotal - all except Exploration		\$ 57,810,438	
Subtotal - Exploration		\$ 18,686	
Subtotal - all		\$ 57,829,124	
Contingency (Mining)	30%	\$ 17,343,132	Enter reason here if contingencygreater than default is entered
Contingency (Exploration only)	15%	\$ 2,803	Enter reason here if contingencygreater than default is entered
Contingency Total		\$ 17,345,934	
Grand Total (excluding GST)		\$ 75,175,058	

Contingency for mining activities ok
Contingency for exploration activities ok
